

**First Congregational Church  
Nantucket, MA  
Tower Restoration and Conservation**

**Followup Report**

**August 17, 2011**

**David M. Hart, AIA  
DMH Enterprises, Architects  
104 Federal Street  
Salem, MA 01970  
978 745 2172  
[davidatsalem@comcast.net](mailto:davidatsalem@comcast.net)**

**Portion of SECTION 09910 – HISTORIC PAINTING – Revised 12/26/2007:**

**PAINT SCHEDULE**

**All paint systems shall be three coats minimum or additional coats as required to completely cover.**

**2. Exterior wood and all miscellaneous painted surfaces. The paint schedule refers to products by Fine Paints of Europe.**

**1st Coat: Fine Paints of Europe Oil Primer/Undercoat**

**2nd Coat: Fine Paints of Europe Eurolux Housepaint.**

**3rd Coat: Same as second coat.**

**3. Exterior copper roofing surfaces. The paint schedule refers to products by Fine Paints of Europe.**

**Fine Paints of Europe Keyprimer**

**Fine Paints of Europe Eurolux Housepaint Same as second coat.**

**Alternate using Sherwin Williams products:**

**First, wash with water soluble cleaner such as TSP solution, and rinse with water.**

**1st Coat: Sherwin Williams Kem Kromik Universal Metal Primer white**

**2nd Coat: Sherwin Williams Sher Cryl HPA High performance Acrylic Gloss Extra White**

**3rd Coat: Same as second coat.**

**Portion of SECTION 09910 – HISTORIC PAINTING – Revised 12/26/2007:**

**106 JOB CONDITIONS:**

**A. Do not apply exterior paint materials during the months of November through April. Do not apply exterior paint materials when the temperature of surfaces to be painted and the surrounding air temperatures are below 50 degrees F. or expected to drop below 50 degrees F. for 48 hours after application, or above 85 degrees F.**


**Contractor must furnish and use a hand held moisture meter to determine the moisture content of wood surfaces. Wood surface must have a reading of 15% or less at all times during painting. Contractor shall record each day's moisture level readings, including location of reading.**

**B. Do not apply paint materials in snow, rain, fog, or mist, or when the relative humidity exceeds 80% or to damp or wet surfaces.**

**Meeting 6/5/2008: Weather conditions: 60's Fog, PC**

**Meeting 6/24/2008: Weather conditions: 60's F, PC TStms**

*Note 6 from 6/24/2011 Meeting at site:* Although it is anticipated that all work will be complete before July 3, it was remarked that all work should be done properly, and that if weather or other conditions prevented the work from being done properly, it should be delayed rather than “rushed” just to complete the job.

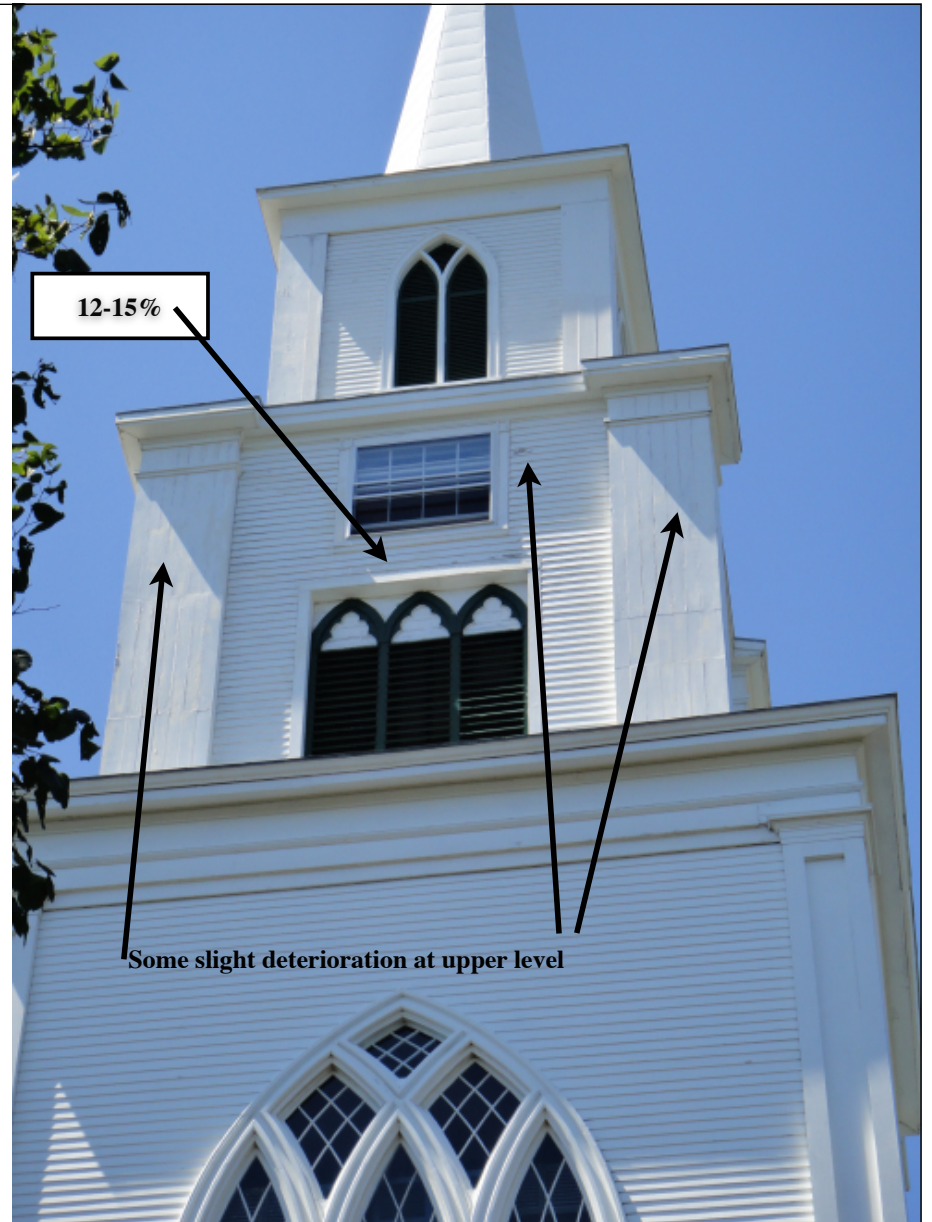

**12-15%** = Moisture readings with hand held moisture meter

**East facade**

DSC01365  
DSC01366



**North facade**

**DSC01357  
DSC01358**



32% One spot

Some slight deterioration at corner board



25 - 32%

Some slight deterioration at upper level

South facade

DSC01363  
DSC01364



**Exterior and interior window sash and trim appear to be intact.**

**South facade**

**DSC01367**

**DSC01368**
